

Bond Street station eastern ticket hall works update


CSJV, Crossrail's contractor for the Bond Street project, would like to take this opportunity to update you on works taking place at the eastern ticket hall site.

Construction of the ventilation shaft – concreting works ('jumpform')

We will commence the construction of the ventilation shaft by the end of November/early December. The shaft will be approximately 30 metres in height once complete and will be included within new buildings due to be constructed by Great Portland Estates. Please see image below. The works will be split into nine concrete pours. The first pour will finish at approximately 7 metres high and will be constructed using traditional methods. The remainder of the structure will be constructed in sections approximately 3 metres in height, allowing the concrete to cure and a new frame to be built on top of it until it reaches the final height of the shaft. This method is referred to as jumpform.

The noise levels will be similar to current levels. We will use a skip to pour the concrete, which is a quieter method than using a pump. The number of deliveries will increase.

The works will be carried out from the end of November/early December 2017 to approximately February 2018. These activities depend on the weather and project progress, and if conditions are not favourable the dates will be subject to change. Respite periods of Monday – Friday 10:00 – 12:00 and 14:00 – 16:00 will be in place for these works.

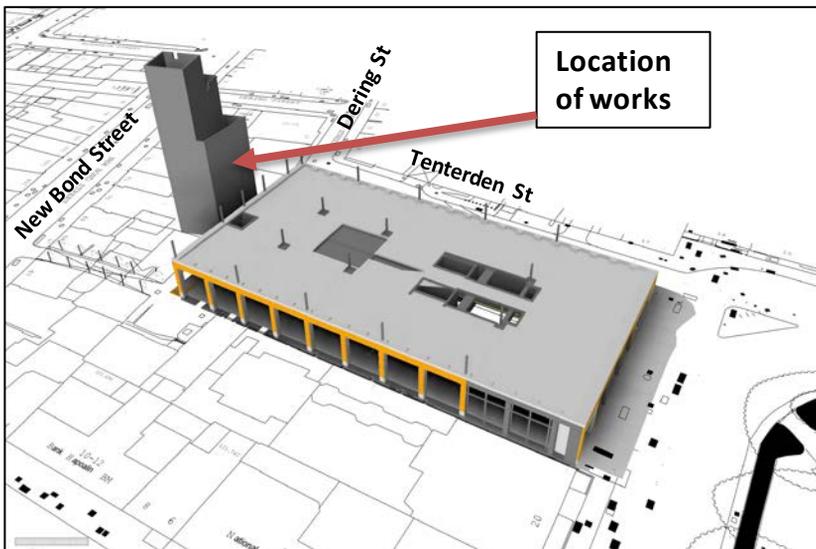

Duration of Works

- Ventilation shaft construction, end of November/early December 2017 – February 2018
- Working hours 24/7. Respite periods Monday – Friday 10:00 – 12:00 and 14:00 – 16:00

What to expect

- Construction of the ventilation shaft
- Delivery and pouring of concrete
- Using a crane to lift materials

What we will do

- Ensure that all personnel accessing and exiting the site are respectful of local businesses and residents, at all stages of our works
- Monitor the perimeter hoarding and footpaths to ensure they are kept clean and well lit
- Security guards will be operational throughout the period
- Monitor dust and noise while keeping within permitted levels set by the Westminster City Council
- Deliveries will be coordinated to avoid congestion

